

RAPPORT DE CHANTIER

n° DRIRE : 304/02/2019

POMPAGE PAR PALIERS

Niveau départ : - 28,18 m
 Hauteur du repère : + 0,70 m
 Refoulement : 200,00 m
 Heure déb : 14h28
 Heure fin : 15h15


Palier 1			
Temps	ND	Débit	Remontée
3mn	31,825	15,70	27,321
4mn	31,766		28,406
6mn	31,805		28,652
8mn	31,844		28,578
10mn	31,883		28,511
15mn	31,969		28,376
20mn	32,024		28,282
30mn	32,074		28,162
40mn	32,120		28,080
50mn	32,120	15,70	28,018
60mn	32,120		27,970

Palier 2 ; Niv. Départ : -27,50 m			
Temps	ND	Débit	Remontée
3mn	35,325	35,20	29,493
4mn	35,469		29,703
6mn	35,737		29,407
8mn	35,914		29,145
10mn	36,051		28,955
15mn	36,325		28,636
20mn	36,527		28,433
30mn	36,795		28,200
40mn	36,978	35,20	28,060
50mn	37,095		27,971
60mn	37,185		27,905

Palier 3			
Temps	ND	Débit	Remontée
3mn	38,800		31,207
4mn	39,115	50,10	30,811
6mn	39,516		30,231
8mn	39,761		29,880
10mn	39,971		29,639
15mn	40,313		29,227
20mn	40,609		28,959
30mn	40,971		28,641
40mn	41,186		28,445
50mn	41,337	50,10	28,313
60mn	41,450		28,227

Palier 4			
Temps	ND	Débit	Remontée
3mn	43,040		32,470
4mn	43,524	70,00	31,934
6mn	44,023		31,202
8mn	44,389		30,751
10mn	44,674		30,432
15mn	45,158		29,907
20mn	45,528		29,569
30mn	45,950		29,141
40mn	46,211		28,885
50mn	46,395	70,00	28,710
60mn	46,547		28,577

Pompage par paliers sur le forage de l'EARL LEVEQUE à Rocourt Saint Martin les 17 et 18/12/2019

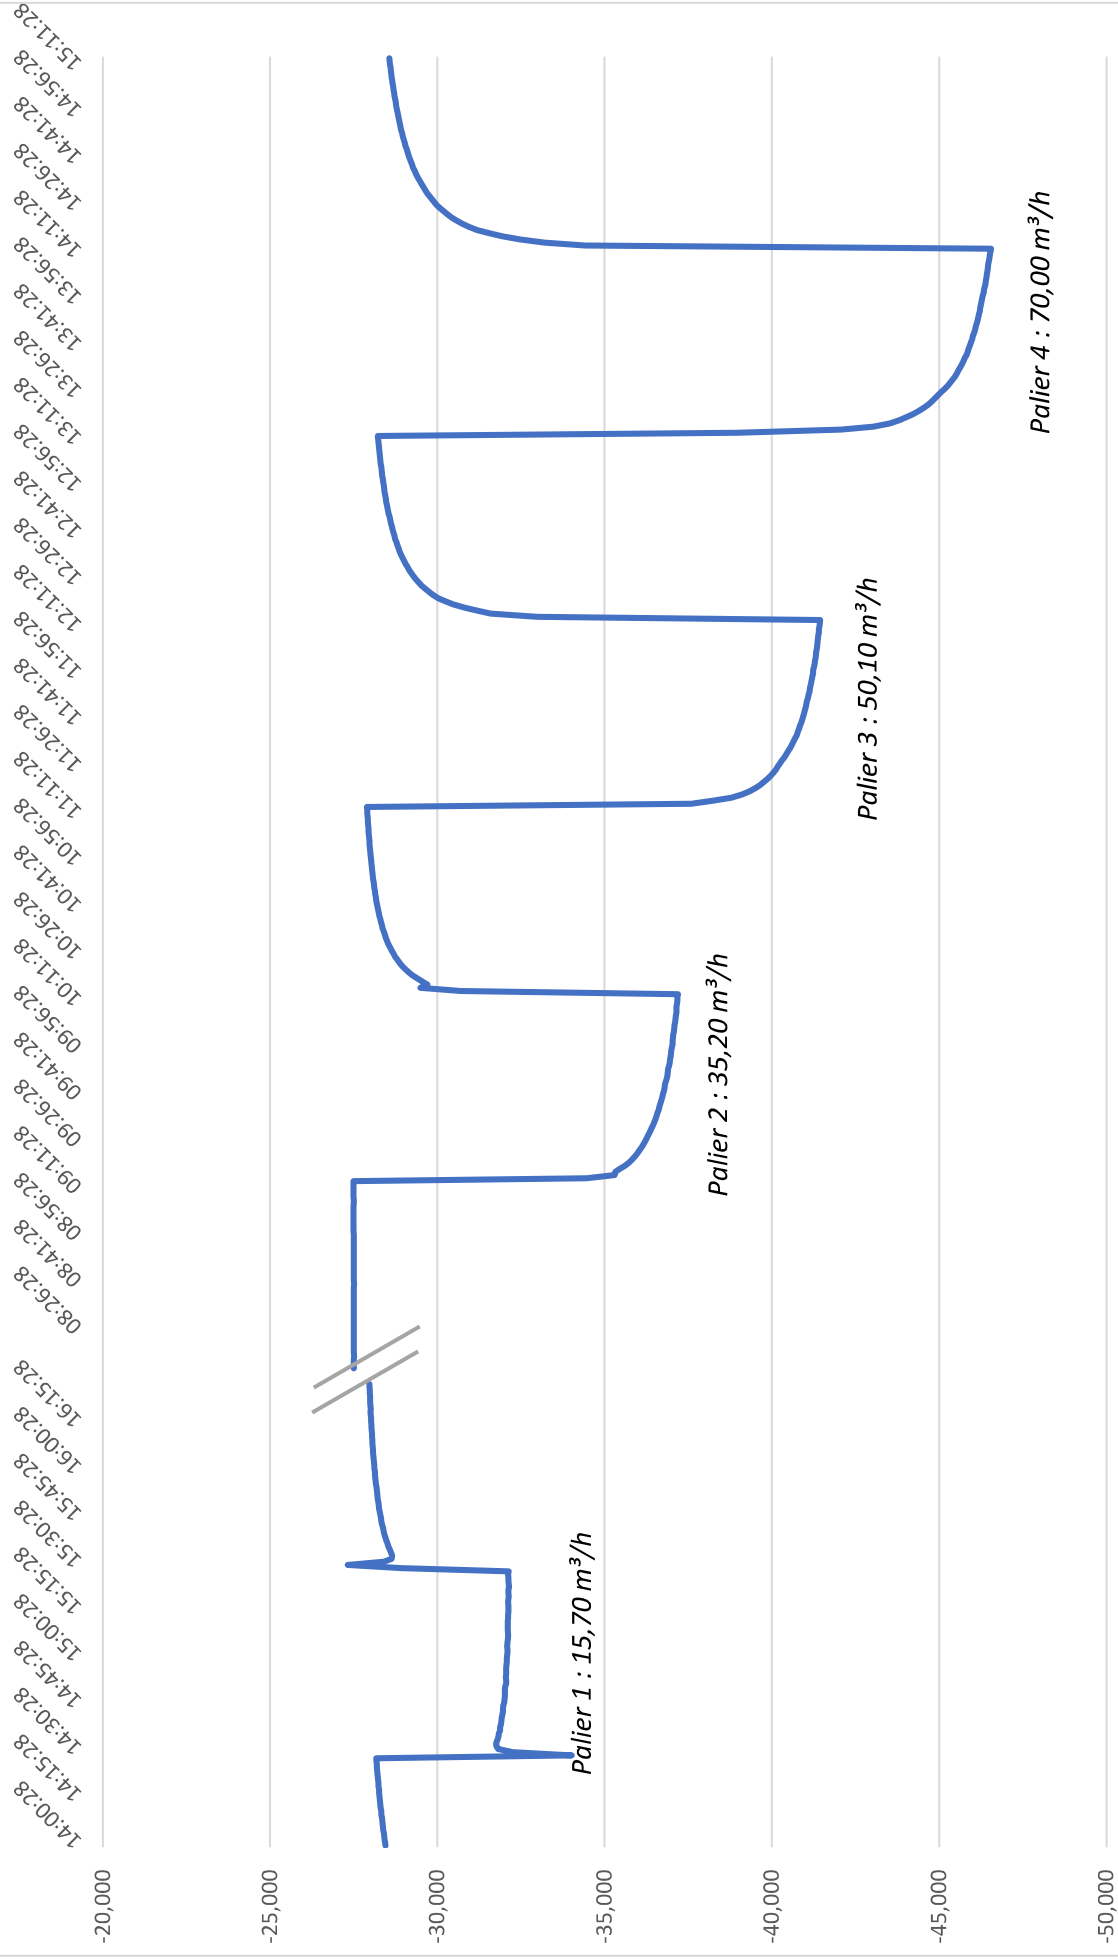

RAPPORT DE CHANTIER

POMPAGE DE LONGUE DUREE

				Niveau départ :		- 28,36 m		
Heure déb :		15h39		Hauteur du repère :		+ 0,70 m		
Heure fin :		15h44		Refoulement :		200,00 m		
Descente				Remontee				
Temps		ND	Debit	Obs.	Temps		Forage	Obs.
1mn		34,963			1mn		40,034	
1mn30			61,00		1mn30			
2mn		39,612			2mn		35,395	
2mn30					2mn30			
3mn		40,847			3mn		34,601	
3mn30					3mn30			
4mn		41,404			4mn		34,018	
4mn30					4mn30			
5mn		41,739			5mn		33,606	
6mn		41,969			6mn		33,295	
7mn		42,167			7mn		33,046	
8mn		42,308			8mn		32,840	
9mn		42,444			9mn		32,641	
10mn		42,541			10mn		32,490	
12mn		42,725			12mn		32,241	
14mn		42,904			14mn		32,038	
16mn		43,044			16mn		31,871	
18mn		43,512			18mn		31,724	
20mn		43,703			20mn		31,595	
25mn		43,941			25mn		31,335	
30mn		44,124	61,00		30mn		31,130	
45mn		44,475			45mn		30,693	
1h		44,701			1h		30,401	
1h30		44,986			1h30		30,020	
2h		45,173			2h		29,760	
3h		45,415			3h		29,407	
4h		45,587			4h		29,153	
5h		45,723			5h		28,966	
6h		45,833			6h		28,815	
7h		45,919			7h		28,690	
8h		46,004			8h		28,581	
9h		46,071			9h		28,492	
10h		46,137			10h		28,414	
12h		46,243			12h		28,278	
15h		46,360			15h		28,111	
18h		46,449			18h		27,994	
21h		46,535	61,00		21h			
24h		46,590			24h			

Pompage de 24h à 61,00 m³/h sur le forage de l'EARL LEVEQUE à Rocourt Saint Martin du 18 au 20/12/2019

